

# WEST SHORE LAKE PONTCHARTRAIN STAKEHOLDER UPDATE

## MAY 2024

L. Jeff Williams  
Senior Project Manager, WSLP  
New Orleans District  
U.S. Army Corps of Engineers



U.S. ARMY



US Army Corps  
of Engineers®



# AGENDA

- Resiliency Study Schedule
- Construction Status and Photos/Videos
- Tentative Delivery Plan & Design Status

<https://www.mvn.usace.army.mil/About/Projects/West-Shore-Lake-Pontchartrain/>



# RESILIENCY STUDY SCHEDULE

DATE	MILESTONE
February 27, 2023	Feasibility Cost Share Agreement (FCSA)
July 17, 2023	Alternatives Milestone Meeting (AMM)-120 days
December 5, 2025	Tentatively Selected Plan (TSP)
January 28, 2026	Release Draft Report and Draft EIS/EA for Concurrent Review
June 29, 2026	Agency Decision Milestone (ADM)
May 25, 2028	Chief's Report



# CONSTRUCTION STATUS

- WSLP-110 contract was awarded on 21 Dec 22
  - 79% Scheduled; 82% Completed
- WSLP-107 contract was awarded on 15 Mar 23
  - 46% Scheduled; 46% Completed
- WSLP-101a contract was awarded on 28 April 23
  - 36% Scheduled; 33% Completed
- WSLP-108 contract was awarded on 25 August 23
  - 31% Scheduled; 28% Completed
- WSLP-104 contract was awarded on 25 August 23
  - 15% Scheduled; 16% Completed
- WSLP-106 contract was awarded on 9 September 23
  - 26% Scheduled; 26% Completed




# CONSTRUCTION STATUS

- WSLP-102 contract was awarded on 14 September 23
  - 16% Scheduled; 17% Completed
- WSLP-105 contract was awarded on 22 September 23
  - 12% Scheduled; 12% Completed
- **Pile Load Test Contract**
  - ▶ Prescott Site: Completed
  - ▶ I-55 Site: Completed
  - ▶ Reserve Relief Site: Completed



# WSLP - Construction Status

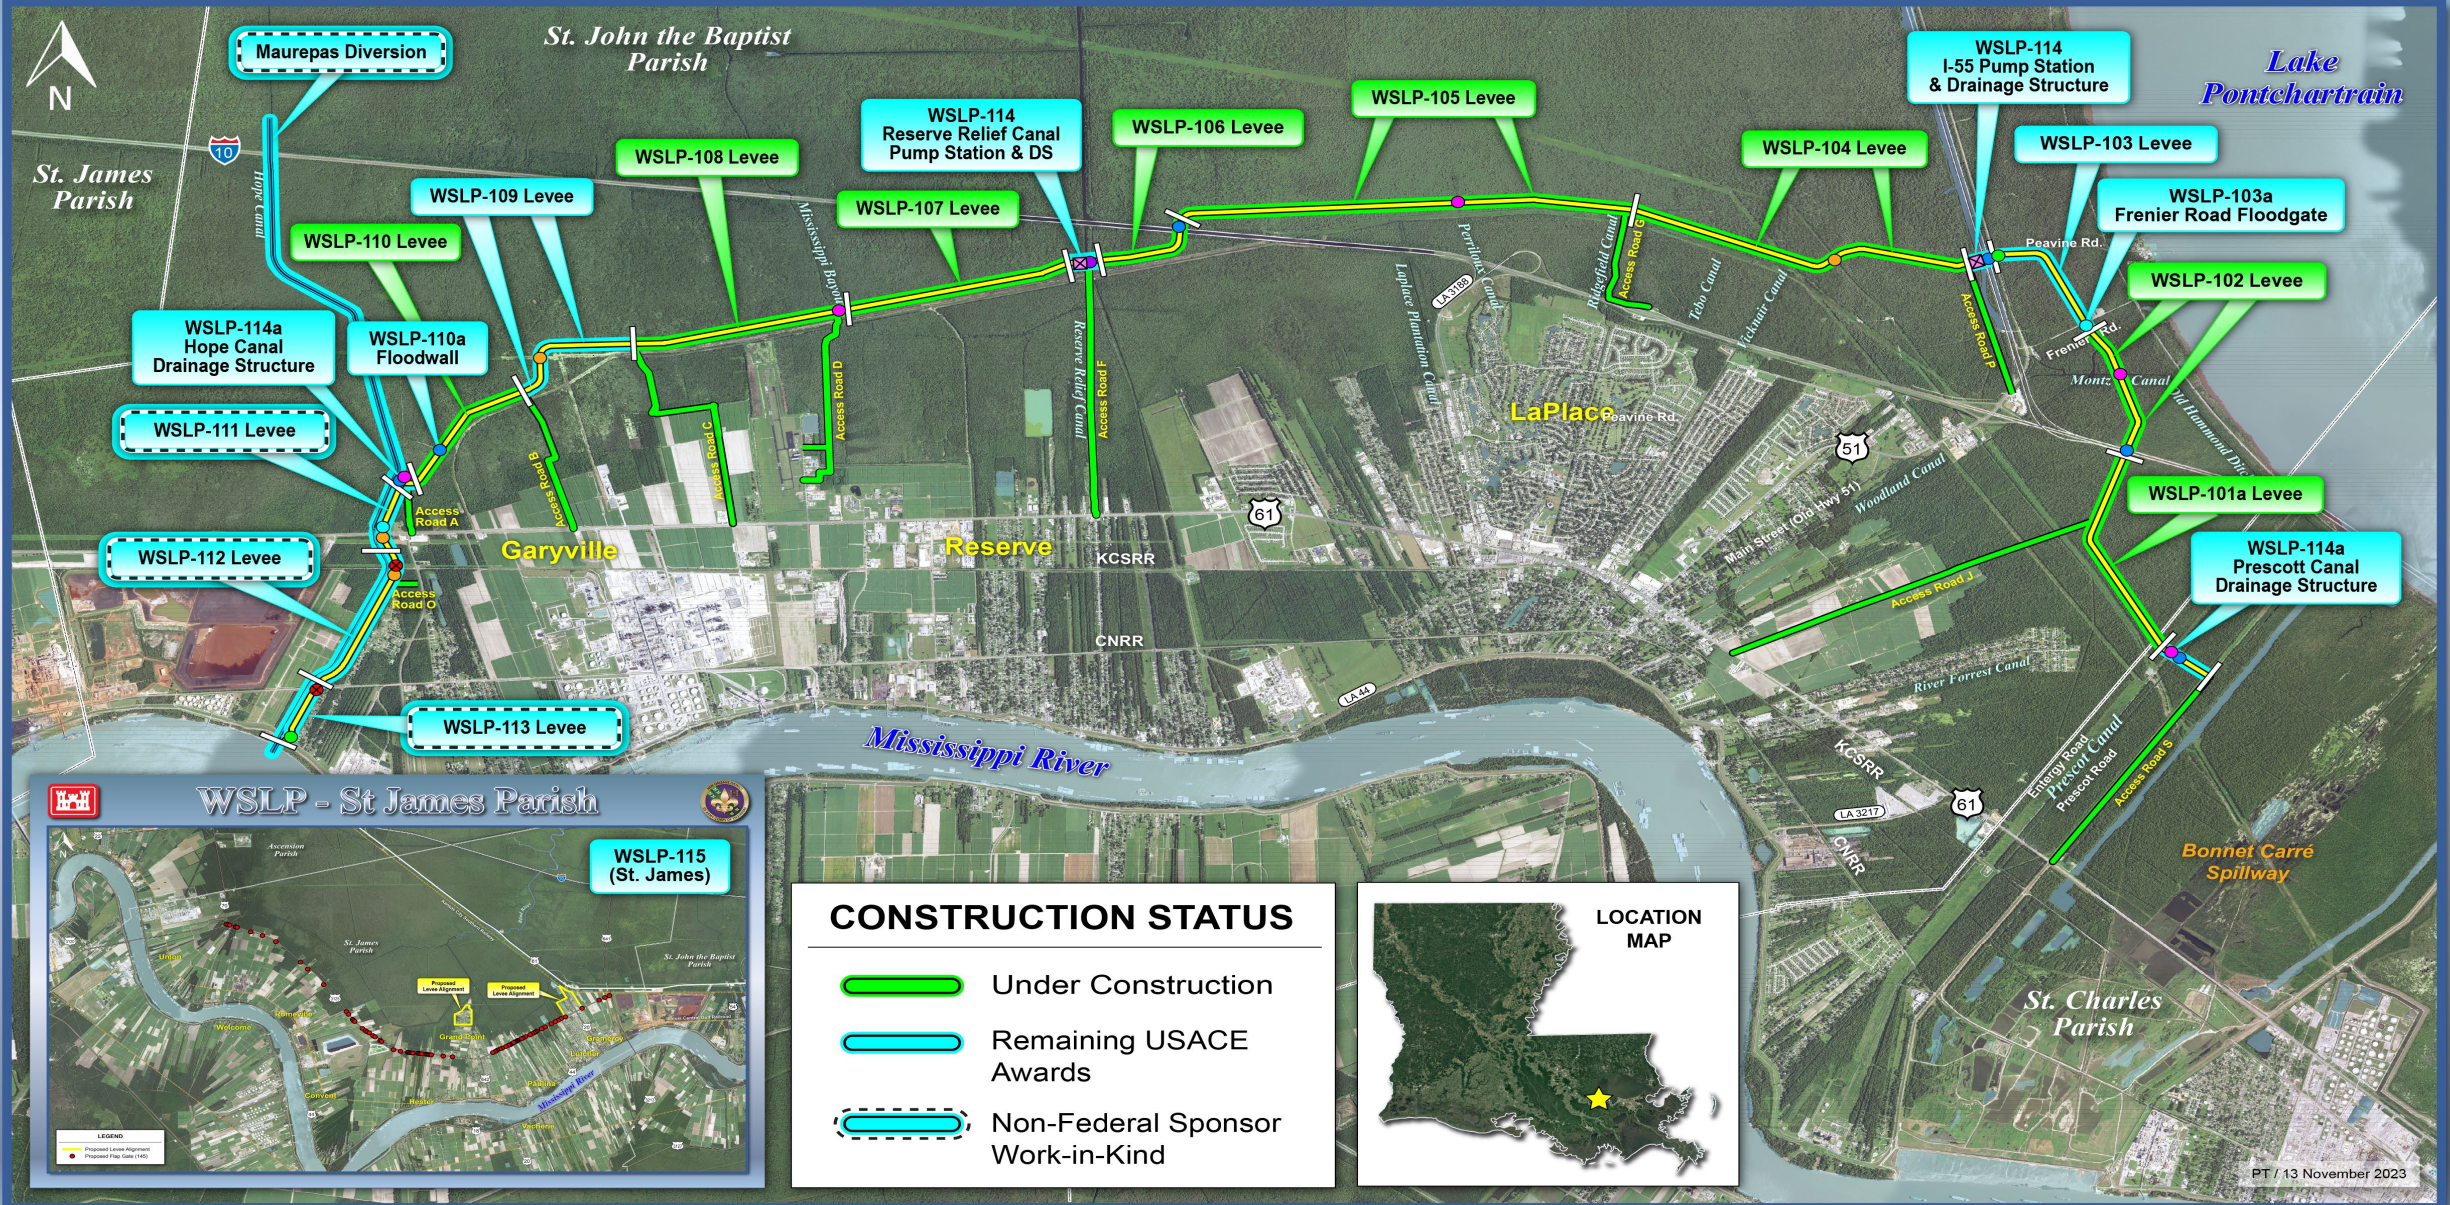

# CONSTRUCTION PHOTOS



WSLP-110 Construction Progress



U.S. ARMY



US Army Corps  
of Engineers

# CONSTRUCTION PHOTOS



WSP-107 Construction



U.S. ARMY



US Army Corps  
of Engineers®



# CONSTRUCTION PHOTOS



WSLP-106 Construction



U.S. ARMY



US Army Corps  
of Engineers®

# CONSTRUCTION PHOTOS



WSLP-102 Construction



U.S. ARMY



US Army Corps  
of Engineers®

# CONSTRUCTION PHOTOS



WSLP-108 Construction



US Army Corps  
of Engineers®

U.S. ARMY




U.S. ARMY



US Army Corps  
of Engineers®

# PRELIMINARY LEVEE CONSTRUCTION SCHEDULE

- Existing elevation approx. -1 feet
- 2023 and 2024: Construct 3-foot sand base and begin levee construction
- 2024: Levee built to heights around +6 feet
- 2025: Levee built to heights ranging +6.6 to +12.5 feet
- 2026: Levee built to full heights

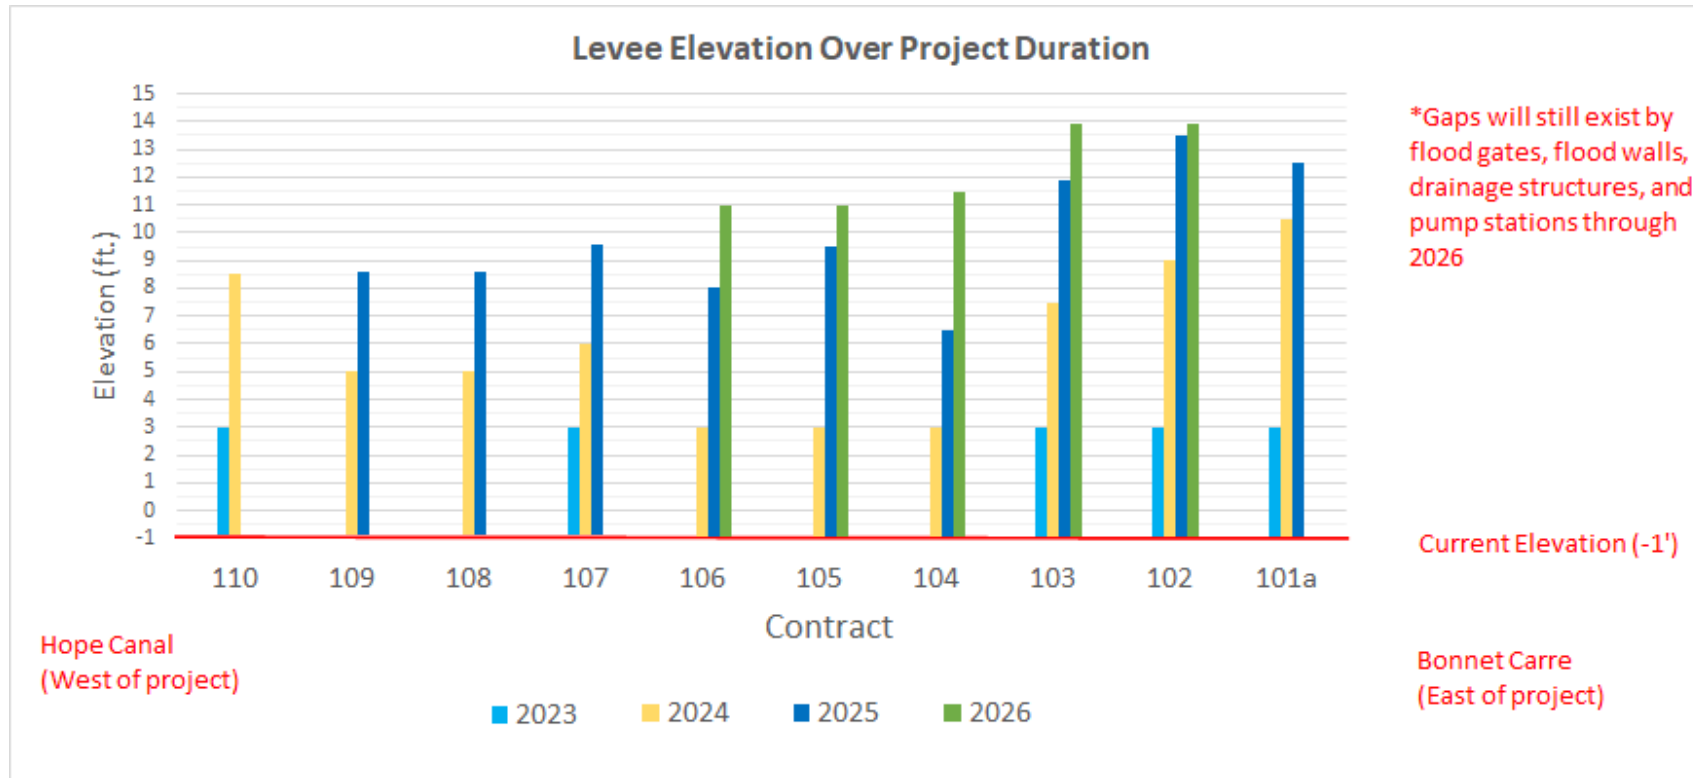



U.S. ARMY



US Army Corps  
of Engineers®

# WEST SHORE LAKE PONTCHARTRAIN TENTATIVE DELIVERY PLAN


Contract ID	Description	Award
WSLP 103	Levee (approx. 1.0 mi.), Floodwall (approx. 500 ft)	21 May 2024
WSLP 109	Levee (approx. 1.0 mi), (approx. 500 ft), Utility Crossings	3Q 2024
WSLP 111**	Levee (approx. 0.5 mi), Highway Ramp, Utility Crossings	
WSLP 112**	Levee (approx. 1.0 mi), Rail Road Gate, Floodwall (approx. 500 ft), Utility Crossings	
WSLP 113**	Levee (approx. 0.5 mi), Floodwall (approx. 500 ft), Rail Road Gate	
WSLP 114	Pump Stations (2 – 2,000 cfs)	1Q 2025
WSLP 114a	Hope and Prescott Drainage Structures	3Q 2024

Note: Project requirements and completion dates may be subject to change as designs are refined and impacts quantified.

\*\*Designed and constructed by CPRA



# West Shore Lake Pontchartrain

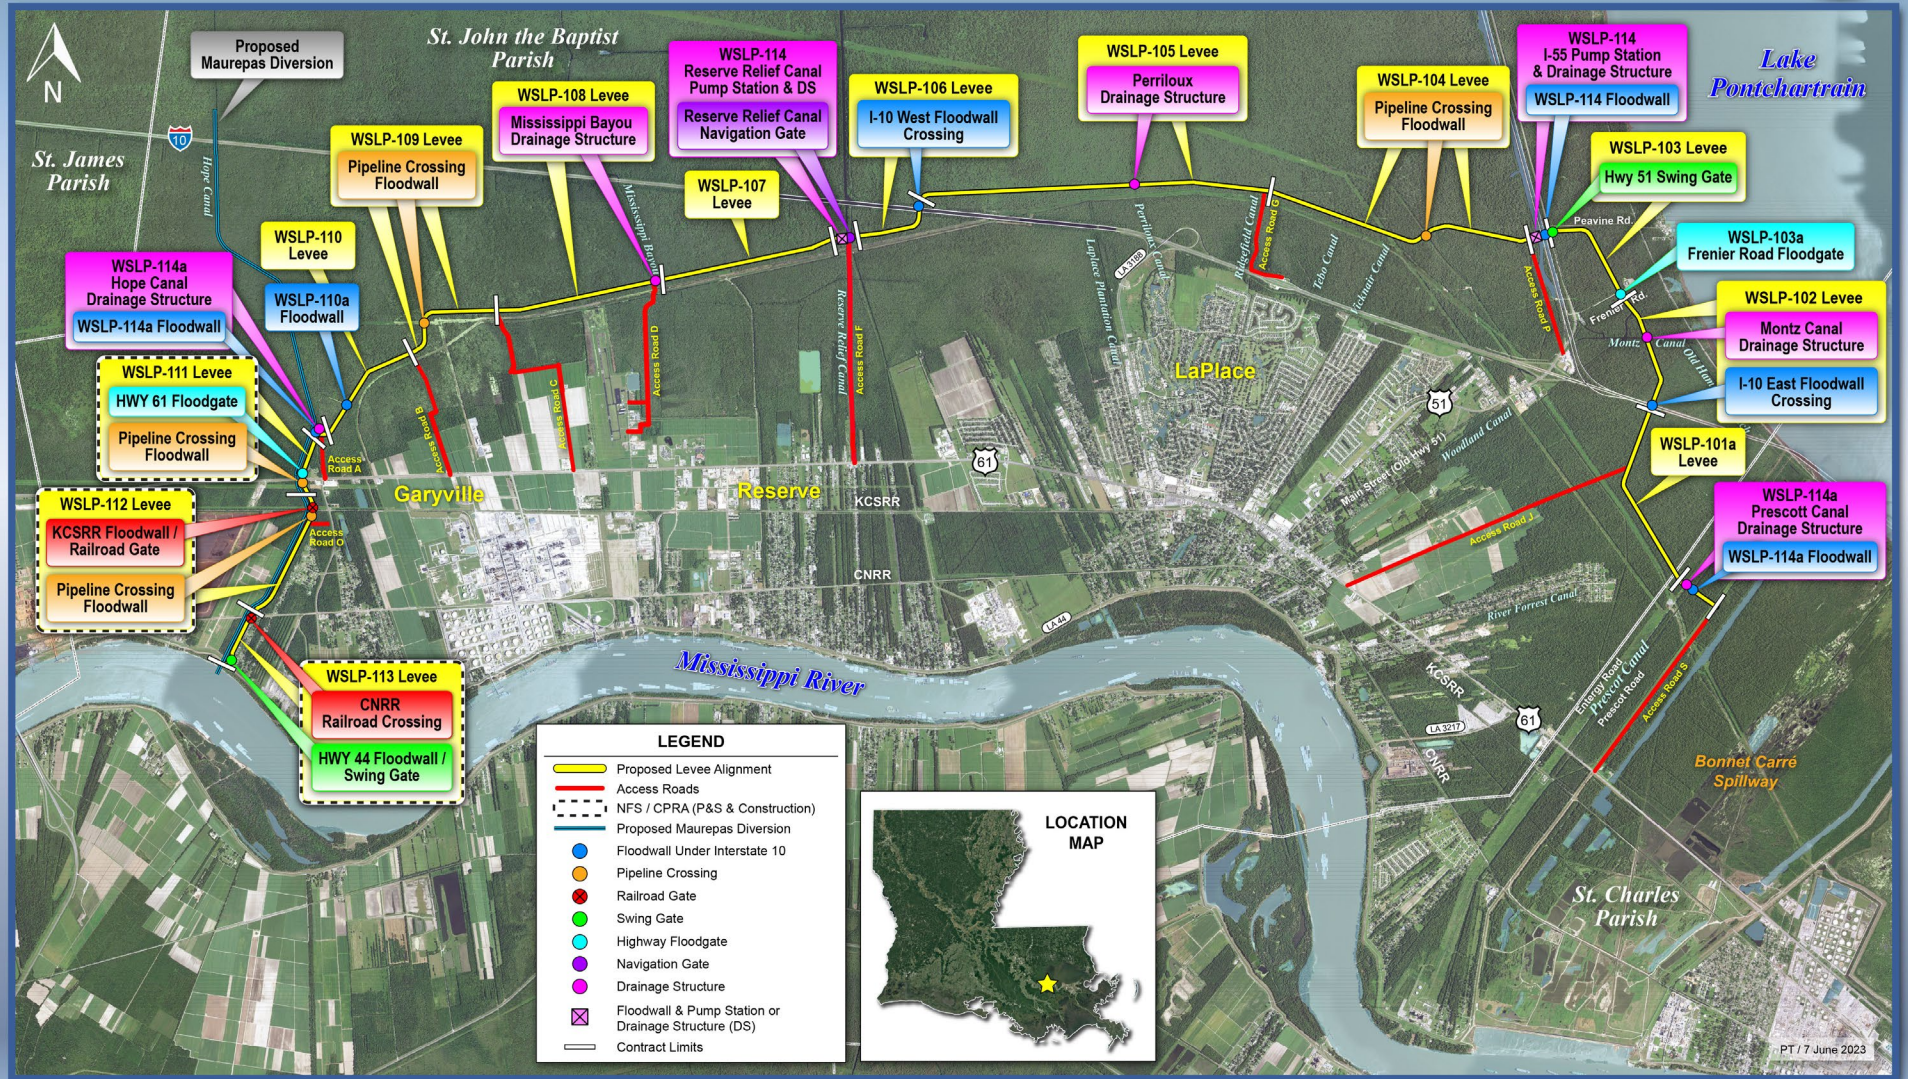

US Army Corps of Engineers

U.S. ARMY



# WSLP - St James Parish



US Army Corps  
of Engineers

U.S. ARMY

# Questions



US Army Corps  
of Engineers®

U.S. ARMY
