

WEST SHORE LAKE PONTCHARTRAIN STAKEHOLDER UPDATE

August 2026

Arielle Gingrow, P.E.

Senior Project Manager

Lake Pontchartrain and Vicinity Branch

New Orleans District

U.S. Army Corps of Engineers



U.S. Army
Corps of Engineers®

U.S. ARMY



AGENDA

- Maps
- Construction Status
- Construction Photos
- Pre-Construction Status
- Maurepas and St. James

<https://www.mvn.usace.army.mil/About/Projects/West-Shore-Lake-Pontchartrain/>




WSLP - St. Charles and St. John Features



Contract Award: 114 & 103A	Contract Award: MD-111, -112, & -113	Contract Award: 110A	Contract Award: 110A, 114A & MD-112	Contract Award: 114, MD-111 & MD-113
Construction Complete: 101A & 110	Construction Complete: 102, 106, 107, 108, & 109	Construction Complete: 103, 103A, 104, & 105	Construction Complete: 110A, 114A & MD-112	Construction Complete: 114, MD-111 & MD-113



WSLP St. John-St. Charles Storm Risk Reduction System Complete





Construction Progress

- 13 of 14 contracts awarded, ~\$1.16B obligated
- Pump station contract awarded April 2026
- 103a awarded July 2026
- 110a to be awarded in FY-28




U.S. ARMY



US Army Corps
of Engineers®



Design and Construction Status St. John and St. Charles Features

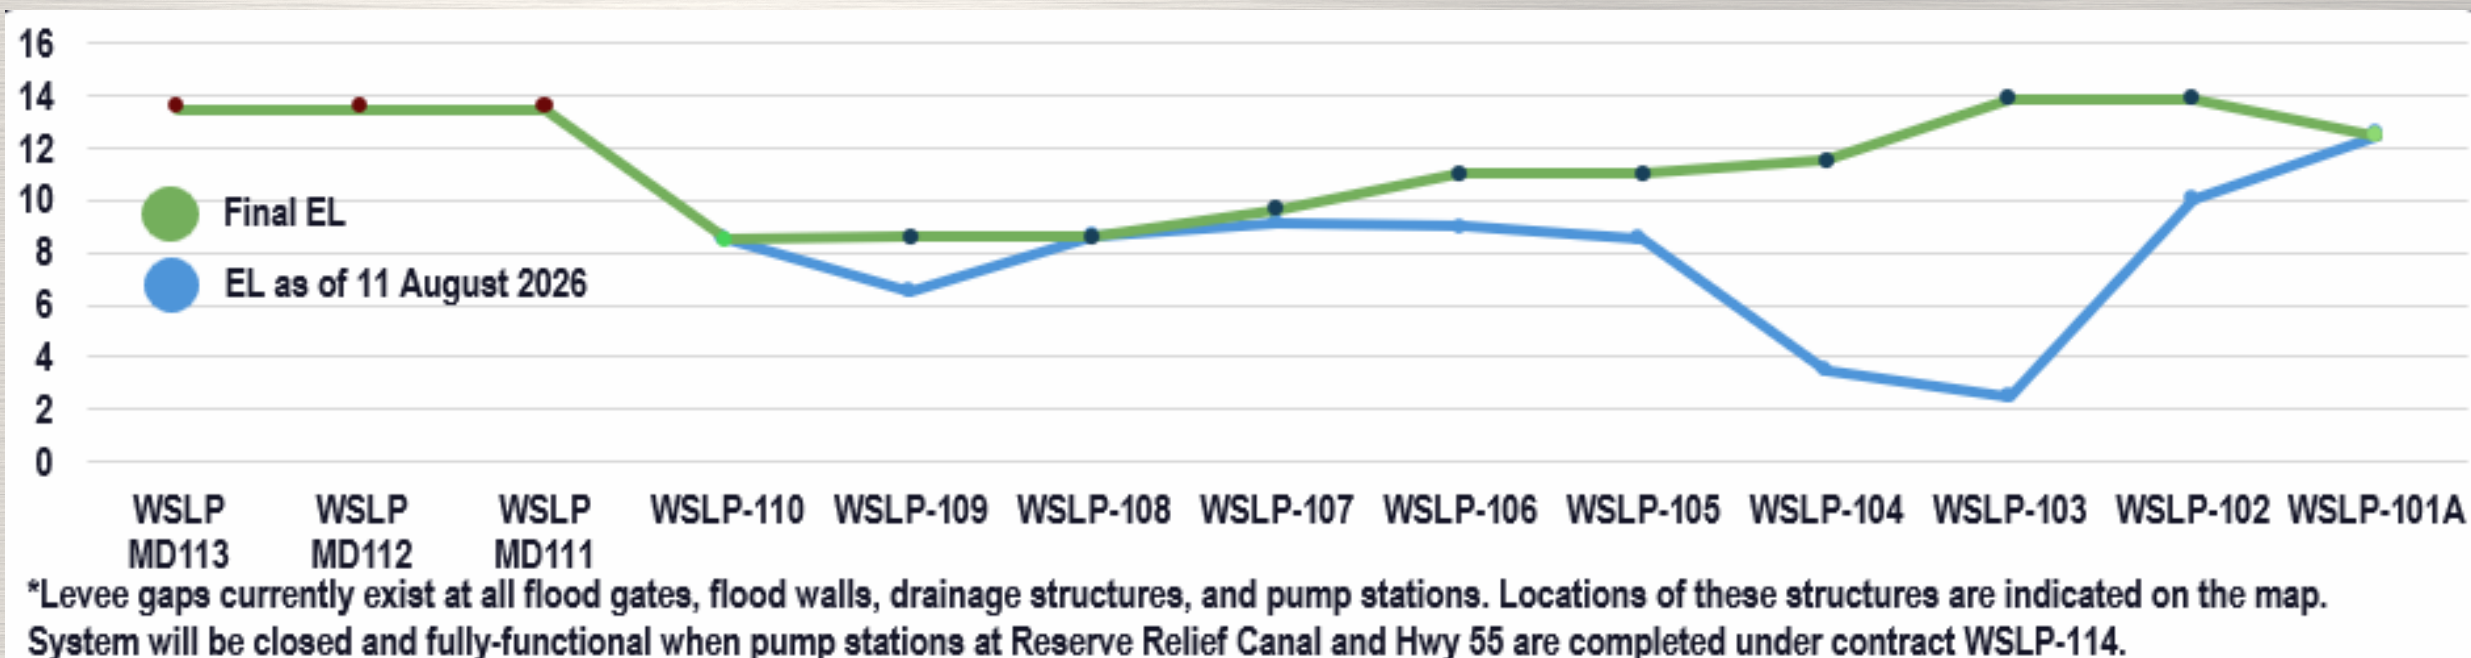


U.S. ARMY



US Army Corps
of Engineers®




CONSTRUCTION STATUS

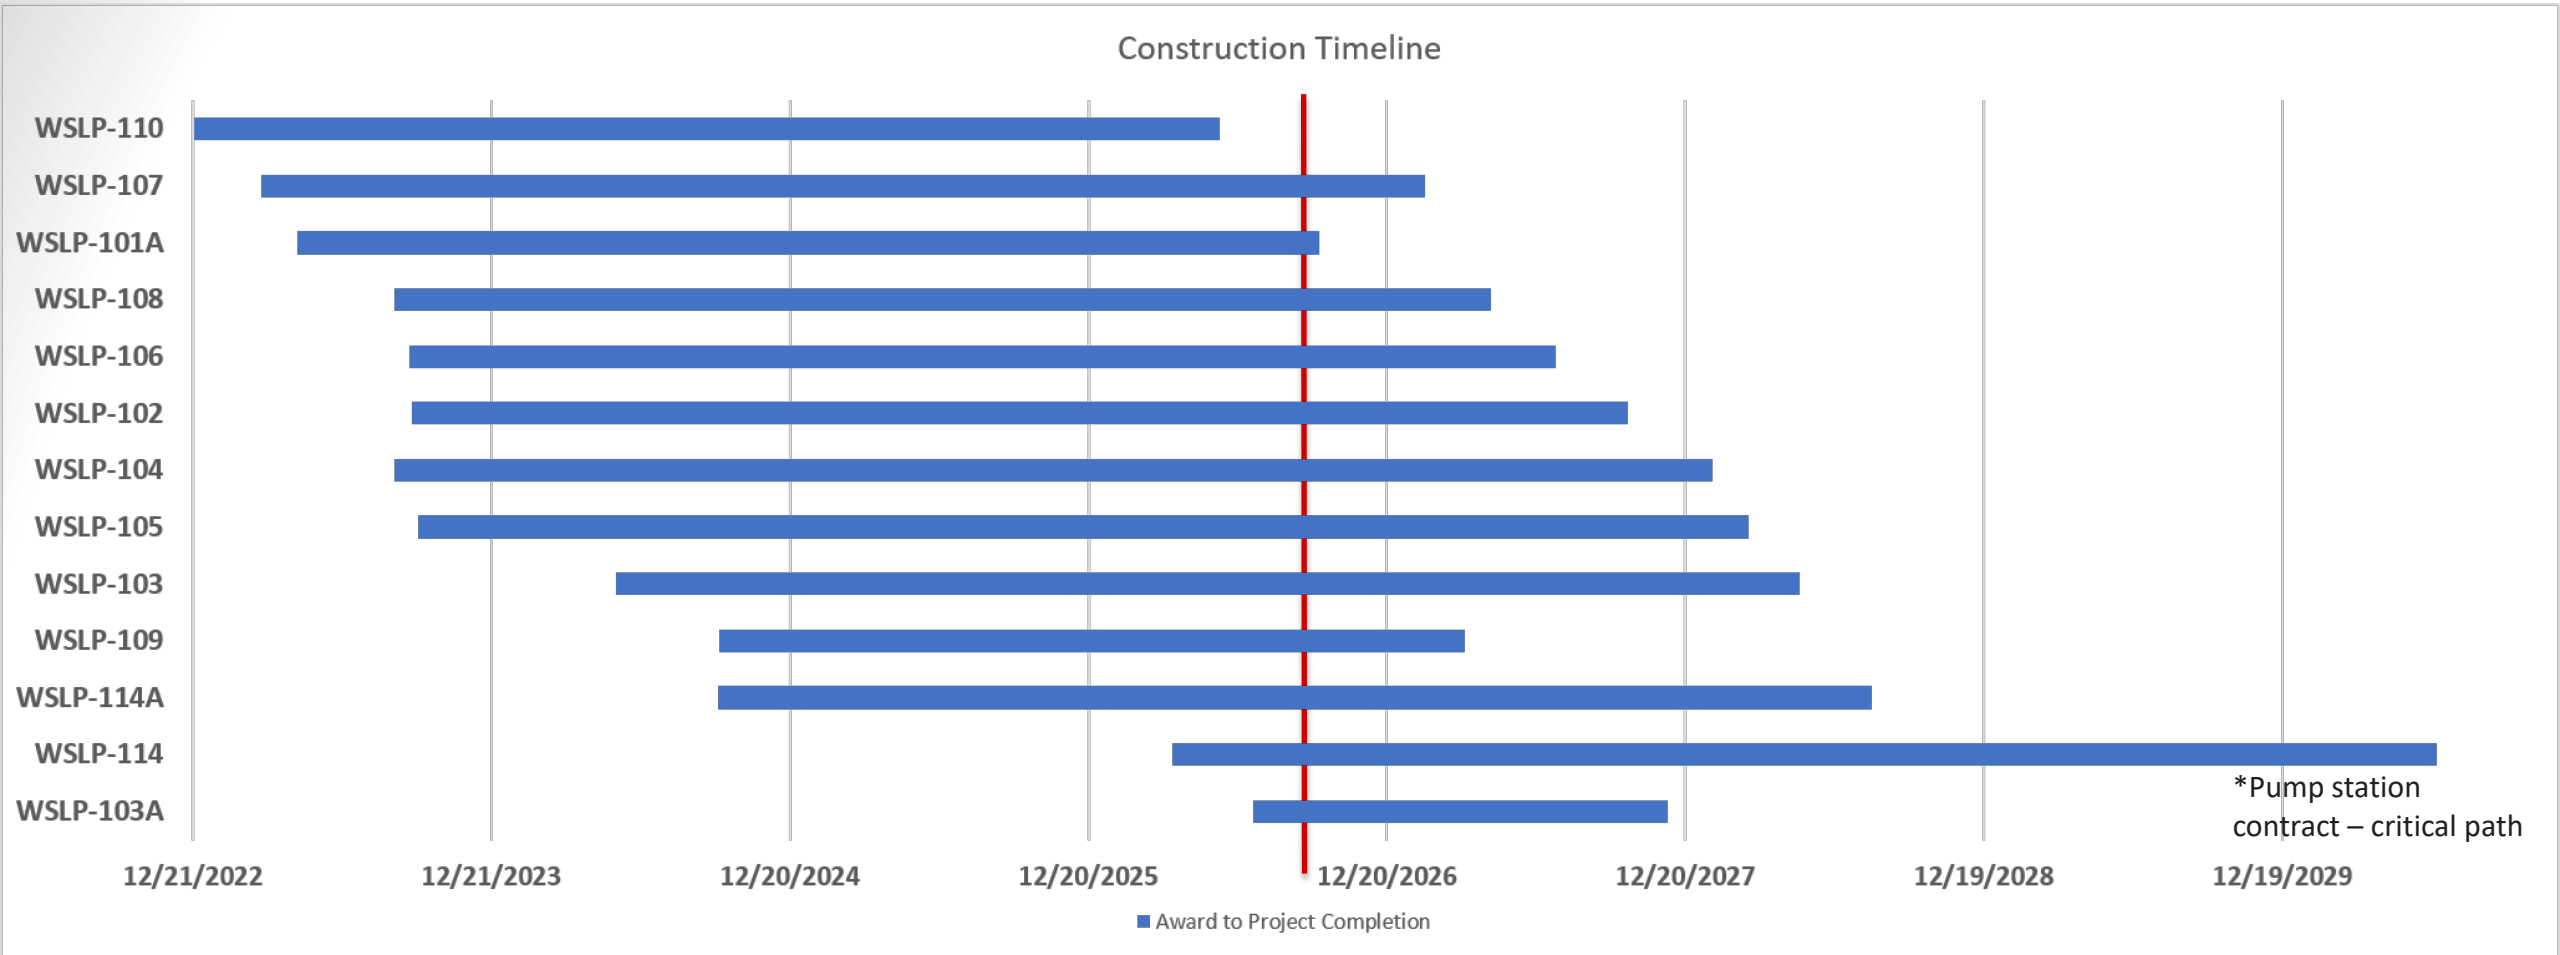



CONSTRUCTION STATUS

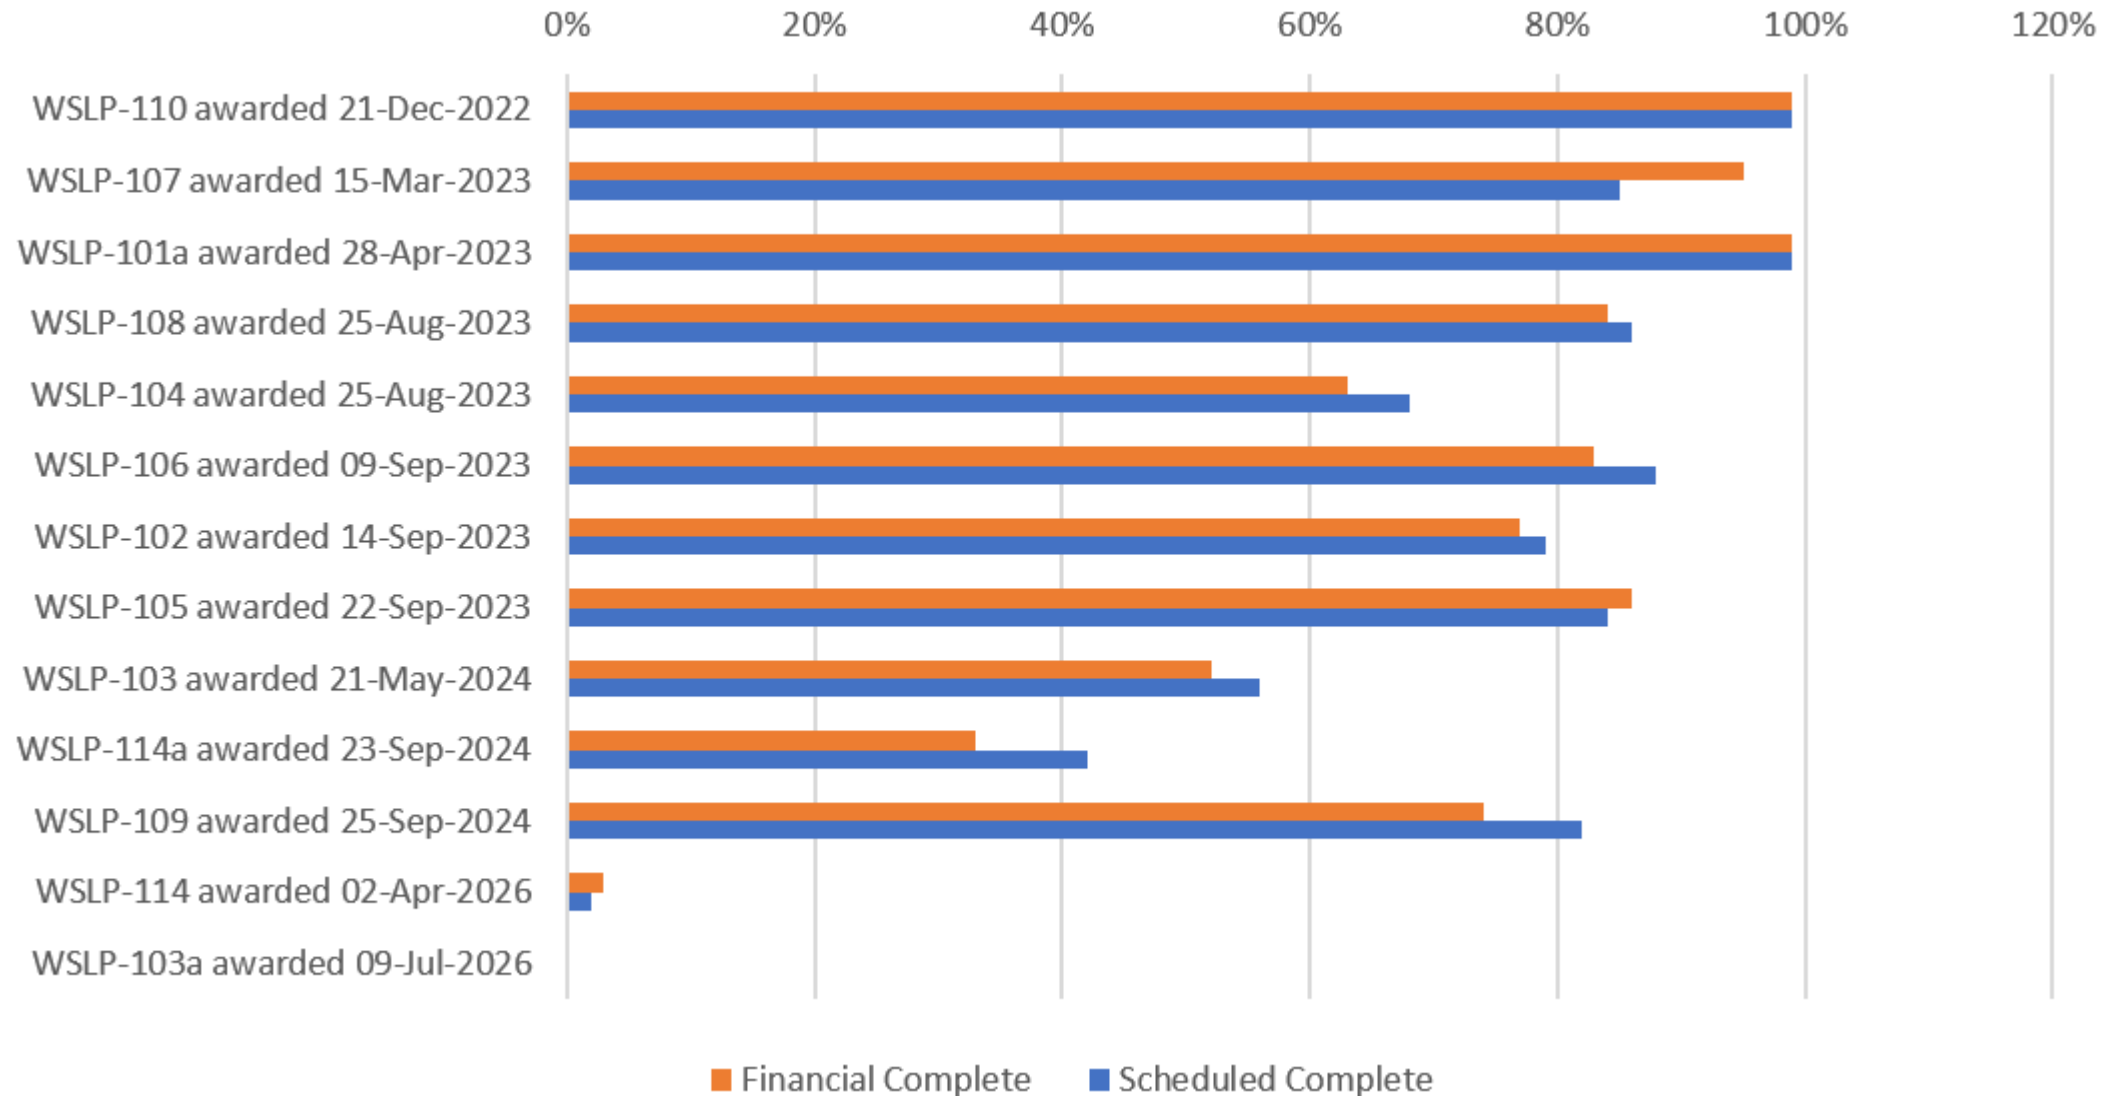

CONSTRUCTION PHOTOS



WSLP-101a Construction



U.S. ARMY



US Army Corps
of Engineers®

CONSTRUCTION PHOTOS



WSLP-102 Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-103 Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-103a Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



U.S. ARMY



US Army Corps
of Engineers®

WSLP-104 Construction

CONSTRUCTION PHOTOS



WSLP-105 Construction



U.S. ARMY



US Army Corps
of Engineers®

CONSTRUCTION PHOTOS



WSLP-106 Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-107 Construction



U.S. ARMY



US Army Corps
of Engineers®

CONSTRUCTION PHOTOS



WSLP-108 Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-109 Construction



US Army Corps
of Engineers®

U.S. ARMY

CONSTRUCTION PHOTOS



WSLP-110 Construction



U.S. ARMY



US Army Corps
of Engineers®

CONSTRUCTION PHOTOS



WSLP-114a Construction



US Army Corps
of Engineers®

CONSTRUCTION PHOTOS



WSLP-114 Construction



US Army Corps
of Engineers®

U.S. ARMY



PRE-CONSTRUCTION STATUS MAUREPAS DIVERSION CONTRACTS AWARDED BY CPRA



- **WSLP-111: Levee from US-61 Raised Hwy Crossing to KCS RR**
 - Current Status: 65% P&S Complete
 - Contract Advertised: January 2028
 - Contract Award: February 2028

- **WSLP-112: Levee from KCS RR to CN RR**
 - Current Status: 95% P&S Complete
 - Contract Advertised: March 2027
 - Contract Award: April 2027

- **WSLP-113: Levee from CN RR to Mississippi River Levee Tie-In at River Road**
 - Current Status: 95% P&S Complete
 - Contract Advertised: March 2027
 - Contract Award: April 2027





PRE-CONSTRUCTION STATUS ST. JAMES CONTRACTS

- Identified initial contracts:
 - WSLP-201: Gramercy Levee**
 - WSLP-202: Grand Point Levee**
- USACE is evaluating options to the authorized project in St. James based on optimizing constructability and cost and responding to changing site conditions: St. James Parish applied for and was approved for a permit to build a levee and water control structures along the M2 Canal.



White: Authorized Project
Yellow: Current Option Being Evaluated
Purple: St. James Parish Connector Levee

Questions



US Army Corps
of Engineers®

U.S. ARMY



West Shore Lake Pontchartrain



St. James Parish Alignment

St. John Parish Alignment

